


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Jan 8, '24									
								S	M	T	W	T	F	S	S	M	
1			House Service Connections St John and Plainfield Between Webster and Matson	4 days	Mon 1/8/24	Fri 1/12/24											
2			Main Connection Monticello	0.8 days	Wed 1/10/24	Wed 1/10/24	1										
3			Main Connection Superior East and West	0.9 days	Wed 1/10/24	Wed 1/10/24											
4			Main Connection Lansdowne East and West	0.8 days	Thu 1/11/24	Thu 1/11/24	3										
5			Main Connection O'Leary West St John West	1 day	Mon 1/15/24	Tue 1/16/24	4										
6			Main Connection Webster and Matson	0.9 days	Tue 1/16/24	Tue 1/16/24											
7			Restoration Plainfield Webster to Matson, St John and Dearborn	3 days	Wed 1/17/24	Mon 1/22/24											
8			Tentatively Schdueld Tie on Plainfield North and South of Schenck	0.9 days	Tue 1/23/24	Tue 1/23/24											
9			House service Connections on Plainfield between Matson and Galbrath	4.9 days	Wed 1/24/24	Wed 1/31/24											

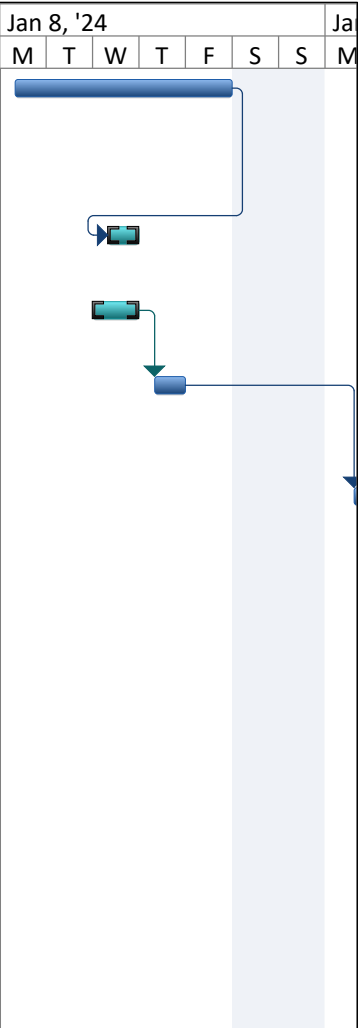

Project: Deer Park Estimate
Date: Mon 1/8/24

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Jan 8, '24							Ja	
								S	M	T	W	T	F	S		S
10		Tie in Plainfield North of Matson Tie in Plainfield at Hoffman	0.9 days	Thu 2/1/24	Thu 2/1/24											
11		Tie in Plainfield at Oakwood and Tie in Plainfield South of Galbrath	0.9 days	Mon 2/5/24	Mon 2/5/24											
12		Resoration Plainfield between Oakwood and Galbrath	2 days	Wed 2/7/24	Fri 2/9/24											
13		Tie in Plainfield at Linden Ave	0.9 days	Tue 2/13/24	Tue 2/13/24											
14		House service Connections Plainfield North of Galbrath	3 days	Wed 2/14/24	Mon 2/19/24											
15		Tie in Plainfield at Galbrath and Plainfield North of Linden	0.9 days	Tue 2/20/24	Tue 2/20/24											
16		Restoration Plainfield North of Galbrath	3.3 days	Tue 2/20/24	Fri 2/23/24											
17		Permanent Restoration will be Completed in Late Spring														

Project: Deer Park Estimate
Date: Mon 1/8/24

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	
